

 PEAK PAINTING & DECORATING

GUIDE 1 OF 2 · DESKTOP

How to use Peak Paint OS.

The office side, one screen per page. Guide 2 covers the app the crew carry on site.

FOR THE TRIAL

Danny — work through it in order with a real job. Each page ends with the one question I want your answer to. Where it does not match how Peak actually works, write on the page.

Two front doors, one set of numbers.

You work in HQ on the desktop. The crew work in the app on their phones. Nothing is entered twice — what they mark off on site is what your reports and invoices are built from.

HQ · DESKTOP · THIS GUIDE	FIELD · PHONE · GUIDE 2
Settings & rates library	Clock on and off
Quotes	Sign on to the SWMS
Projects & schedule	Mark off progress
Health & Safety	Photos
Variations & materials	Flag a variation
Timesheets	Request materials
Invoicing	Quick quote from site
Reports & KPIs	

01	Settings & rates	05	Variations & materials
02	Quotes	06	Timesheets
03	Projects & schedule	07	Invoicing
04	Health & Safety	08	Reports & KPIs

THE ONE-LINE VERSION

Price from the rates library, let the crew mark off what they have painted, and the report, the claim and the invoice build themselves.

Set these two up first.

Settings prints on every PDF the system makes. The rates library prices every quote, quick quote and variation.

SETTINGS → COMPANY DETAILS

Company / trading name

PEAK PAINTING & DECORATING LTD

Issued by (name)

The Bro #4

Role / title

Director / PM

Address

Unit 2, 8 Husheer Place

Suburb / city

Onekawa, Napier 4110

Region / country

Hawke's Bay · New Zealand

Email

quotes@peakpainting.co.nz

Phone

+64 27 555 0148

GST number

123-456-789

Bank account (shown on invoices)

02-0630-0123456-00

Fill it once — it carries onto quotes, invoices, H&S packs and reports.

RATES LIBRARY

CODE	ITEM	UNIT	BASE RATE (EX-GST)	LOADING FACTOR	CHARGE-OUT (LOADED)
WASH	Exterior wash · moss & mould Resene Deep Clean	m²	\$ 3.5	Ground floor · ×1.00	\$3.50 incl GST \$4.02
				Sound / new · ×1.00	
PREP-INT	Interior prep · fill, sand, spot-prin incl. materials	m²	\$ 6	Ground floor · ×1.00	\$6.00 incl GST \$6.90
				Sound / new · ×1.00	
PREP-EXT	Exterior prep · scrape, sand, gap· incl. materials	m²	\$ 9.5	Ground floor · ×1.00	\$9.50 incl GST \$10.92
				Sound / new · ×1.00	
PRIME-T	Prime bare timber Resene Quick Dry	m²	\$ 7.5	Ground floor · ×1.00	\$7.50 incl GST \$8.63
				Sound / new · ×1.00	
STAINB	Stain block / seal Resene Sureseal	m²	\$ 6.5	Ground floor · ×1.00	\$6.50 incl GST \$7.47
				Sound / new · ×1.00	
INT-CEIL	Ceiling · 2 coats Resene SpaceCote Flat	m²	\$ 17	Ground floor · ×1.00	\$17.00 incl GST \$19.55
				Sound / new · ×1.00	

One line per thing you sell. Base rate is your cost-plus starting point; the loading factor produces the charge-out rate that quotes actually use.

Your call, Danny: are these the right rate lines and loadings for Peak, and is anything you price regularly missing from the library?

Build a quote from rate lines.

Quotes → **New quote.** Enter client and site, then add a line per rate code and type the quantity.
Nothing is priced by hand.

THE PRICED LINES

LINE ITEM	UNIT	QTY	RATE	TOTAL
Walls · 2 coats · \$22/m²	m²	210	\$22.00	\$4,620
Ceiling · 2 coats · \$17/m²	m²	140	\$17.00	\$2,380
Interior prep · fill, sand, spot-prime · \$6/m²	m²	210	\$6.00	\$1,260
Skirting / architrave · 2 coats · \$8/lm	lm	120	\$8.00	\$960

Quantity × charge-out rate = line total. Change a quantity and the totals move with it. First four of this quote's seven lines shown.

Subtotal	\$12,698
Discount	-\$0
Net	\$12,698
GST 15%	\$1,905
Total	\$14,603

THEN

- 1 Write the inclusions and exclusions in plain sentences
- 2 Download the quote PDF and send it
- 3 Set the status to *Sent*, then *Accepted* or *Declined*

Subtotal, discount, net, GST, total — live as you type.

Your call: does the quote PDF read the way you want a Peak quote to read, and are the standard exclusions the ones you use?

Accepted quote becomes the job.

The quote total becomes the contract value. From there the project header is the one place that shows where the job stands.

14 Marewa Rd, Napier

In progress

PJ-1042 · Whitfield · Ext + Int repaint

CONTRACT

\$18,450

excl. GST

53% complete

Create report

Site, status, contract value and live percentage complete, with the report and claim buttons on the right.

Contract summary	
Contract value	\$18,450
Variations (draft)	+\$450
Invoiced to date	\$9,225
Balance	\$9,225

Contract summary — value, variations, invoiced to date, balance.

Job schedule · 14–25 Jul

Drag a bar to reschedule · drag its right edge to change duration

	14 MON	15 TUE	16 WED	17 THU	18 FRI	21 MON	22 TUE	23 WED	24 THU	25 FRI
PJ-1042 14 Marewa Rd · Whitfield	B1 · B4 14–17 Jul									
PJ-1035 21 Battery Rd · Harbourview			B2 16–22 Jul							
PJ-1031 3 Latham St · Chen	B3 14–15 Jul									
PJ-1039 8 Kennedy Rd · Ropati			B3 17–22 Jul							
PJ-1028 12 Thackeray St · Douglas						B1 22–24 Jul				

5 jobs · 4 crew · weekends hidden · changes are local to this prototype

Schedule — drag a bar to move the job, drag its edge to change duration. The crew initials on the bar are who sees it on their phone.

Your call: is a week-at-a-time board how you plan crew, or do you need a longer horizon?

Documents out, sign-ons back.

Write the task analysis for the site, generate the SWMS, and it appears on the crew's phones. Their sign-on comes straight back here.

Safety documents

+ Task analysis / JHA

+ SWMS

+ Toolbox talk

+ SSSP

TYPE	DOCUMENT	JOB	ITEMS	STATUS	UPDATED
TA · JHA	Working at height · exterior repaint 1 high-risk · 3 signed on	PJ-1042	4	Active	14 Jul
SWMS	Airless spraying · exterior 2 high-risk · not yet signed	PJ-1035	3	Draft	13 Jul
SSSP	Site-Specific Safety Plan 1 high-risk · 2 signed on	PJ-1035	3	Active	10 Jul
Toolbox	Toolbox talk · w/c 14 Jul 4 attended · 1 action	All sites	2	Signed · 4	14 Jul

Tap a row to open & edit · issued documents show in the field app and the crew acknowledge them at sign-on.

Safety documents for the job — task analysis, SWMS, and the pack to download.

Today's sign-on log

NAME	JOB	SIGNED
The Bro #1	PJ-1042	Today 7:42am
The Bro #2	PJ-1042	Today 7:45am
The Bro #4	PJ-1042	Today 7:42am
The Bro #3	PJ-1039	Today 8:05am

Each sign-on acknowledges the active safety documents for that site.

Today's sign-on log — who signed, which job, what time.

- 1

Pick the hazards for this site from the hazard library
- 2

Generate the SWMS before day one
- 3

Check the sign-on log each morning
- 4

Download the pack when a client or main contractor asks

Your call: does this cover what Site Safe and your main contractors actually ask Peak for?

Extra work, priced and on the record.

The crew flag extra work from site with photos and a rate. It lands on your dashboard to price, approve or decline.

THE REGISTER FOR THE JOB

Variation claims			
AREA	DESCRIPTION	VALUE	STATUS
Kitchen / Dining	Gib repair to water-damaged wall before painting · flagged on site, 2 photos	\$450	Draft on site Send to client
Approved variations add to the contract sum and flow into the next progress claim automatically.			

Area, description, value, status. Approved values are added to the contract sum; drafts are not.

WHAT YOU DO WITH IT

- 1

Open the flagged variation from the dashboard
- 2

Check the photos and the rate, adjust the value
- 3

Approve or decline — approved ones show on the next report
- 4

Materials requests arrive the same way, tied to the job

What the crew fill in on the phone — area, description, a rate from your library, quantity and photos — is shown in Guide 2, page 05.

Your call: should a variation be sendable to the client for written approval before the crew start it?

Approve the week, then export.

Clock-ins arrive from the phones. Overtime past 8 h a day is calculated at 1.5×, vehicle km at \$0.83.

TOTAL HOURS
135.5
134 ord · 1.5 OT

LABOUR COST
\$5,375
wages + OT + vehicle km

CHARGED OUT
\$8,513
at \$75/hr charge rate

LABOUR MARGIN
\$3,137
37% of charge-out

UTILISATION
84%
hours billable to a job

EXCEPTIONS
3
to clear before payroll

The week in six numbers. Utilisation is hours billable to a job over hours paid — the one to watch.

Crew hours

Tap a row for detail

CREW	JOB	MON	TUE	WED	THU	FRI	TOTAL	COST	CHARGE	STATUS
B1 The Bro #1 Leading hand · 46 km	PJ-1042	8	8	8+0.5	7	8	39.5	\$1,549	\$2,963	Approved
B2 The Bro #2 Painter · 28 km	PJ-1035	8	8	6	8	8+1	39	\$1,366	\$2,925	Approved
B3 The Bro #3 Painter · 34 km	PJ-1039	7	8	8*	8*	4	35	\$1,218	\$2,625	Approve
B4 The Bro #4 Director / PM · 118 km	Multiple	4	3	5	4	6	22	\$1,242	non-chargeable	Approved

Overtime auto-calculated at 1.5× past 8 h/day · vehicle km at \$0.83 · approved hours post to job costing and to the payroll export.

Hours by crew and job, with cost and charge-out. Click a row for clock times, breaks and GPS.

Exceptions

clear before payroll

Off-site clock-in

The Bro #2 · Tue

Started 1.2 km from PJ-1035 geofence

Resolve

No clock-out

The Bro #3 · Wed

Auto-closed at 8.0 h — confirm finish time

Resolve

No break logged

The Bro #3 · Thu

8.5 h continuous — breach of break policy

Resolve

Clear these before payroll — missed clock-outs, no break logged, off-site starts.

Labour budget burn

PJ-1042 · Marewa ...

97.5 / 132 h

39.5 h this week

74% · 34.5 h left

PJ-1035 · Battery ...

81 / 88 h

39 h this week

92% · 7 h left

PJ-1039 · Kennedy ...

65 / 64 h

35 h this week

102% · -1 h left

Budget hours come off the quoted take-off, so overrun shows up mid-job — not at invoicing.

Actual hours against the hours you quoted, per job.

Your call: Export gives a payroll CSV, a job-cost CSV, the raw grid and a signed PDF. Which format does your payroll actually need, and are the cost rates and the \$0.83 km rate right?

Claim what the crew have marked off.

Send the progress report first, then raise the claim off the same percentage. The amount is worked out for you.

Invoice schedule				Raise progress claim · \$ 554
#	DESCRIPTION	AMOUNT	STATUS	
INV-01	Deposit · 10% on acceptance	\$1,845	Paid	
INV-02	Progress claim 1 · to 40%	\$7,380	Paid	
INV-03	Progress claim 2 · to 53% complete	\$554	Ready to raise	
INV-04	Final · on completion + variations	\$9,225	Not due	

The claim schedule for the job. **Raise progress claim** arrives pre-loaded with what is owed.

HOW THAT \$554 IS WORKED OUT	
Contract value	\$18,450.00
Complete, from the crew's capture	53%
Earned to date · 53% × \$18,450	\$9,778.50
Less already invoiced	−\$9,225.00
This claim, excl GST	\$553.50


OUTSTANDING \$23,340 3 invoices unpaid	OVERDUE \$2,400 1 follow up	PAID · MTD \$7,400 1 settled	DRAFT \$553 ready to raise
--	-----------------------------------	------------------------------------	----------------------------------

Invoicing across all jobs — outstanding, overdue, paid this month, and drafts ready to raise.


Your call: are your terms and retentions handled the way you need, and should approved variations be claimed separately or rolled into the progress claim?

Nothing here is typed in.

Every figure is built from the jobs, quotes and timesheets already in the system.



Revenue, gross margin, win rate, average job, jobs done, debtor days.

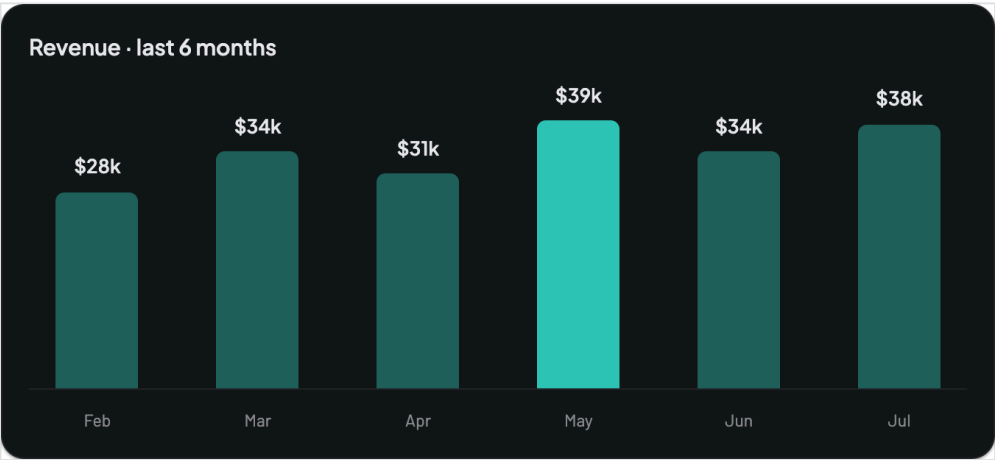

Revenue by month, drawn from invoices raised.

FIGURE	BUILT FROM
Contract value	accepted quote + approved variations
% complete	value-weighted average of each area's captured percentage
This claim	(% × contract value) – previously invoiced
Labour cost	hours × cost rate, OT at 1.5×, plus km at \$0.83
Debtor days	average days from invoice issued to marked paid

Your call: which of these six numbers do you actually run the business on, and what is missing?

What to tell us.

Three things are worth more than a long list: what is missing, what is wrong, and what you would never use.

THE EIGHT QUESTIONS, IN ORDER

- 01 Are the rate lines and loadings right?
- 02 Does the quote PDF read like a Peak quote?
- 03 Is a week-at-a-time schedule enough?
- 04 Does the H&S pack satisfy your contractors?
- 05 Should variations go to the client for approval first?
- 06 Which payroll format do you need?
- 07 Terms, retentions and variation claims — right?
- 08 Which KPIs do you actually run on?
