



GUIDE 1 OF 2 · DESKTOP

How to use Peak Paint OS.

The office side, one screen per page. Guide 2 covers the app the crew carry on site.

FOR THE TRIAL

Danny — work through it in order with a real job. Each page ends with the one question I want your answer to. Where it does not match how Peak actually works, write on the page.


WORKED THROUGH PJ-1042 · WHITFIELD, MAREWA RD

SEPTEMBER 2026 · v2

Two ways in, one system.

Open the link and you land on the sign-in screen. **Management** is the office side — quotes, rates, costs, invoicing and payroll. **Crew** is the same jobs, schedule, H&S and timesheets with the money hidden. Each role can carry a four-digit PIN, set in Settings.

THE SIGN-IN SCREEN

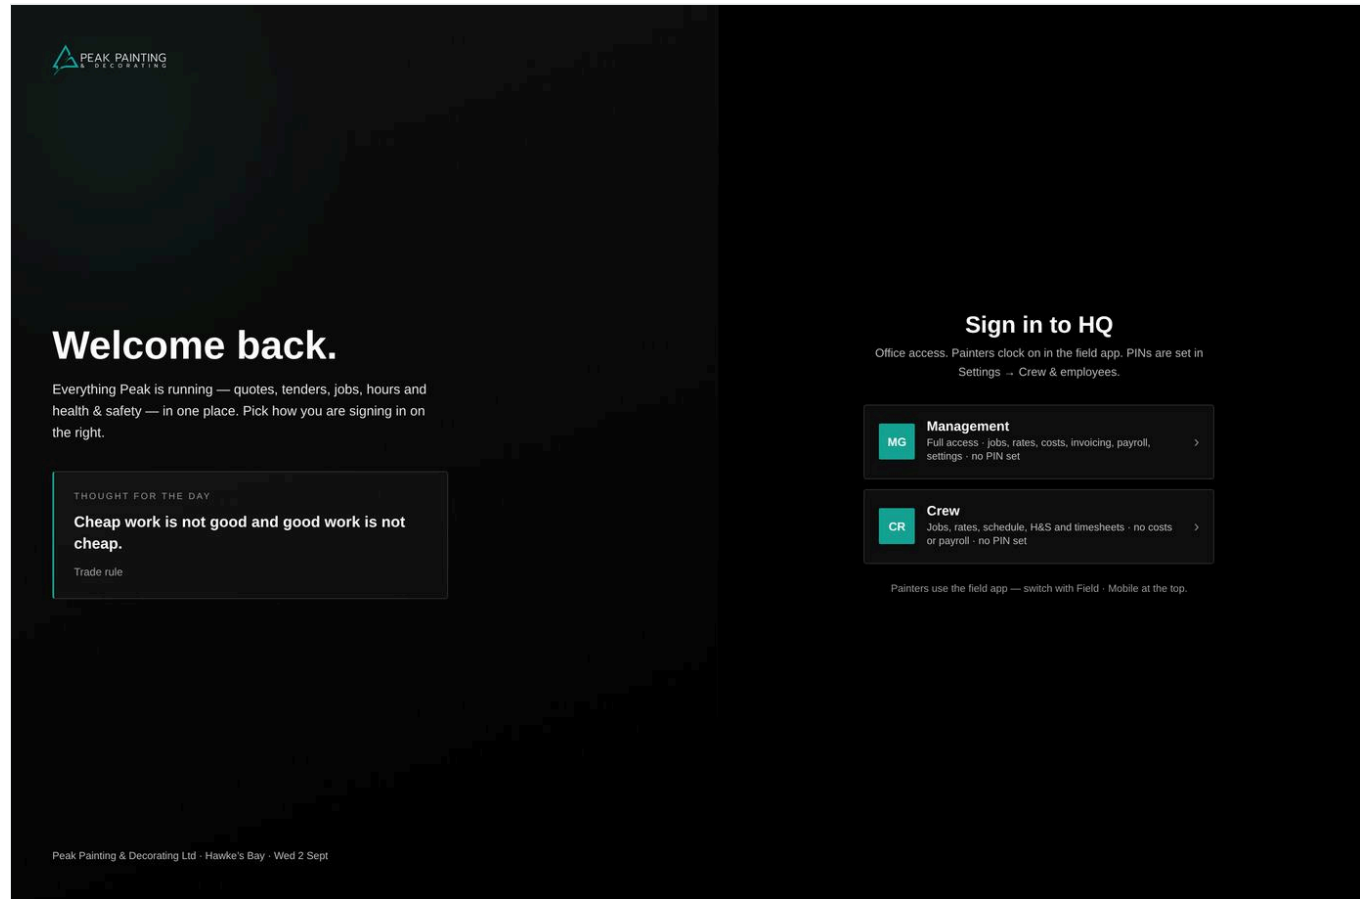

Painters do not use this screen — they use the field app on their phone, covered in Guide 2.

AFTER YOU ARE IN

- 1 The **logo, top left, is the home button** — it returns you to the Dashboard from anywhere, and to this sign-in screen from the Dashboard.
- 2 The **icon rail** down the left is the menu. Hover it and it opens with labels; who you are signed in as, and Sign out, sit at the bottom of it.
- 3 The **light / dark switch** is top right. Crossing to the field app and back always asks for the PIN again.

Your call, Danny: do you want PINs on both roles, or leave Management open on your own machine?

What the day looks like.

One screen: what is live, who is on site, what is waiting on you, and the weather that decides whether tomorrow is an exterior day.

PEAK PAINTING
PROTOTYPE

Light

HQ · Desktop

Field · Mobile

Dashboard

Q Search jobs, clients...

+ New quote

ACTIVE JOBS

2

1 on site today

ON SITE NOW

0

no sign-ons yet today

VARIATIONS TO PRICE

2

+1,575 flagged from site

MATERIALS REQUESTS

1

Ordered - Resene Lustacryl 4L

H&S ACTIONS

3

1 draft to issue - 2 tickets expiring

PAINTING WEATHER · NAPIER

Wed 85% rain — plan an interior day for the crew

Wed 2

13°

5% rain · 12 km/h · 62% RH

Exterior OK

Thu 3

14°

10% rain · 18 km/h · 68% RH

Exterior OK

Fri 4

11°

85% rain · 30 km/h · 91% RH

Interior only

Sat 5

10°

60% rain · 22 km/h · 84% RH

Marginal - pm

Sun 6

12°

5% rain · 14 km/h · 65% RH

Exterior OK

Today on site

Wed 2 Sept - live from clock-ons & the field app

14 Marewa Rd, Napier

PJ-1042 · Whitfield

On site

53%

Painter #1

Painter #2

Danny

Now: Kitchen / Dining — gib repair, then walls

3/3 signed on · TA acknowledged

Open job

Active jobs

View all

JOB	CLIENT	PROGRESS	VALUE	STATUS	PHOTOS	
PJ-1042	14 Marewa Rd, Napier	Whitfield	53%	\$18,450	In progress	+1
PJ-1105	12 Te Mata Rd	S. Keller	20%	\$14,200	Live	—

Needs attention

PJ-1042 · Kitchen / Dining

+ \$450

Flagged by Danny Williams - 2 photos

Draft - on site

Review variation

Decline

PJ-1042 · Soffits & Fascia

+ \$1,125

Flagged by Danny Williams - 4 photos

Draft - on site

Review variation

Decline

H&S · SWMS still in draft

Before spray day

Airless spraying - 14 Marewa Rd — issue to crew before Thursday

Open H&S

Q-2090 · Macleod follow-up

sent 11 Jul

\$26.1k ext + roof - no reply in 3 days — call before it goes cold

Open quotes

Active jobs now carries the latest site photos on the right of each row — tap the job to see the rest.

Your call: are these the five numbers you want across the top, or would you swap one out?

Set these two up first.

Settings prints on every PDF the system makes. The rates library prices every quote, quick quote and variation — nothing is priced by hand.

SETTINGS → COMPANY & CREW

PEAK PAINTING & DECORATING LTD

PROTOTYPE

Office - will sync

Light

HQ - Desktop

Field - Mobile

Company settings

Search jobs, clients...

Company details

These details print on every exported document — quotes, tax invoices, H&S packs and progress reports.

Company / trading name

PEAK PAINTING & DECORATING LTD

Issued by (name)

Danny Williams

Role / title

Director / PM

Address

Unit 2, 8 Husheer Place

Onokawa, Napier 4110

Region / country

Hawke's Bay - New Zealand

Email

quotes@peakpainting.co.nz

Phone

+64 27 555 0148

GST number

123-456-789

Bank account (shown on invoices)

02-0630-0123456-00

PEAK PAINTING & DECORATING LTD

QUALITY / PRECISION / FINISH

DOCUMENT TITLE

PROJECT LOCATION: NZ

SECTION HEADING

REF: 0000

Danny Williams - Director / PM

Unit 2, 8 Husheer Place, Onokawa, Napier 4110

Hawke's Bay - New Zealand

quotes@peakpainting.co.nz - T: +64 27 555 0148

LOCATION: NZ

800 1 800 1100

Literhead preview — the shared template every PDF export uses.

Crew & employees

3 active — these people appear in project setup, the schedule and timesheets.

+ Add employees

ID	NAME	ROLE	APP ACCESS	FIELD PIN	COST RATE / HR	CHARGE-OUT / HR	MARGIN	STATUS	
1	Jay Harris	Foreman / PM	Site manager	1234	\$45 mid	\$ 45	\$ 90 auto 2.0x	50%	Active
2	Danny Williams	Owner / PM	Owner / PM	none	\$60 mid	\$ 60	\$ 120 auto 2.0x	50%	Active
3	Ron Jeremy	Apprentice	Worker	none	\$26 mid	\$ 26	\$ 47 auto 1.8x	45%	Active

HQ access PINs

These unlock the office app. Separate from the field PINs above, which are per

Management PIN

Crew PIN

Company details carry onto quotes, invoices, H&S packs and reports. Crew rates sit below: pick a band per role and the charge-out rate calculates itself.

RATES LIBRARY

PEAK PAINTING & DECORATING LTD

PROTOTYPE

Light

HQ - Desktop

Field - Mobile

Rates library

Search jobs, clients...

+ Add rate

NZ rates library

Search rates...

+ Add rate

Ad

Prep

Interior

Exterior

Roof

Access

Labour

Loading factors

applied per line to reflect the real site — charge-out = base rate × access × condition

ACCESS - PROXIMITY TO WORK FRONT

Ground floor ×1.00

1st floor - ladder ×1.10

2nd storey - scaffold ×1.25

3rd storey - height ×1.45

SUBSTRATE - CONDITION & AGE

Sound / new ×1.00

Weathered ×1.15

Aged - heavy prep ×1.35

Heritage - falling (100yr) ×1.50

Worked example — Weatherboard \$34m² on 3rd-storey scaffold (×1.45) with heritage boards (×1.50) — \$73.95m² ex-GST.

CODE	ITEM	UNIT	BASE RATE (EX-GST)	LOADING FACTOR	CHARGE-OUT (LOADED)
MASH	Exterior wash - moss & mould	m²	\$ 3.5	Ground floor - >1.00	\$3.50
	Resene Deep Clean			Sound / new - >1.00	incl GST \$4.02
PREP-INT	Interior prep - fill, sand, spot-prime	m²	\$ 6	Ground floor - >1.00	\$6.00
	incl. materials			Sound / new - >1.00	incl GST \$6.90
PREP-EXT	Exterior prep - scrape, sand, gap-seal	m²	\$ 9.5	Ground floor - >1.00	\$9.50
	incl. materials			Sound / new - >1.00	incl GST \$10.92
PRIME-T	Prime bare timber	m²	\$ 7.5	Ground floor - >1.00	\$7.50
	Resene Quick Dry			Sound / new - >1.00	incl GST \$8.63
STAINB	Stain block / seal	m²	\$ 6.5	Ground floor - >1.00	\$6.50
	Resene Sureseal			Sound / new - >1.00	incl GST \$7.47
INT-CEIL	Ceiling - 2 coats	m²	\$ 17	Ground floor - >1.00	\$17.00
	Resene SpaceCote Flat			Sound / new - >1.00	incl GST \$19.55
INT-WALL	Walls - 2 coats	m²	\$ 22	Ground floor - >1.00	\$22.00
	Resene SpaceCote Low Sheen			Sound / new - >1.00	incl GST \$25.30

Base rate is your cost-plus starting point. The loading factor produces the charge-out rate quotes actually use — access and substrate condition, per line.

Your call: are these the right rate lines and loadings for Peak, and is anything you price regularly missing?

Charge for the hard ones properly.

Charge-out = base rate × access × condition. A weatherboard at \$34/m² on third-storey scaffold with heritage boards prices at \$73.95/m² without anyone doing sums on site.

PEAK PAINTING
PROTOTYPING

PROTOTYPE

Offline · will sync

Light

HQ · Desktop

Field · Mobile

Rates library

Search jobs, clients...

+ Add rate

NZ rates library

Search rates...

+ Add rate

AllPrepInteriorExteriorRoofAccessLabour

Loading factors applied per line to reflect the real site — charge-out = base rate × access × condition

ACCESS · PROXIMITY TO WORK FRONT

Ground floor ×1.001st floor - ladder ×1.102nd storey - scaffold ×1.253rd storey+ - height ×1.45

SUBSTRATE · CONDITION & AGE

Sound / new ×1.00Weathered ×1.15Aged - heavy prep ×1.35Heritage - falling (100yr+) ×1.50

Worked example — Weatherboard \$34/m² on 3rd-storey scaffold (×1.45) with heritage boards (×1.50) → \$73.95/m² ex-GST.

CODE	ITEM	UNIT	BASE RATE (EX-GST)	LOADING FACTOR	CHARGE-OUT (LOADED)
ACC-SCAF	Scaffold hire allowance per elevation	item	\$ 850	Ground floor · ×1.00 Sound / new · ×1.00	\$850.00 incl GST \$977.50
ACC-EWP	Cherry picker / EWP day rate	day	\$ 480	Ground floor · ×1.00 Sound / new · ×1.00	\$480.00 incl GST \$552.00
ACC-LADD	Ladder & trestle access single storey	m²	\$ 4	Ground floor · ×1.00 Sound / new · ×1.00	\$4.00 incl GST \$4.60
ACC-TOWER	Mobile tower hire per week	week	\$ 220	Ground floor · ×1.00 Sound / new · ×1.00	\$220.00 incl GST \$253.00
ACC-EDGE	Edge protection / handrail scaffold add-on	lm	\$ 28	Ground floor · ×1.00 Sound / new · ×1.00	\$28.00 incl GST \$32.20
ACC-SWING	Swing stage / rope access day rate	day	\$ 780	Ground floor · ×1.00 Sound / new · ×1.00	\$780.00 incl GST \$897.00
ACC-TRAF	Traffic mgmt / footpath closure per day	day	\$ 450	Ground floor · ×1.00 Sound / new · ×1.00	\$450.00 incl GST \$517.50

Access lines price the gear itself — scaffold, EWP, towers, edge protection, swing stage, traffic management and erect/dismantle labour.


Your call: are the access loadings (×1.10 / ×1.25 / ×1.45) close to what the extra time actually costs Peak?

04 · QUOTES

DESKTOP


Build a quote from rate lines.

Quotes → **New quote**. Enter client and site, then add a line per rate code and type the quantity.

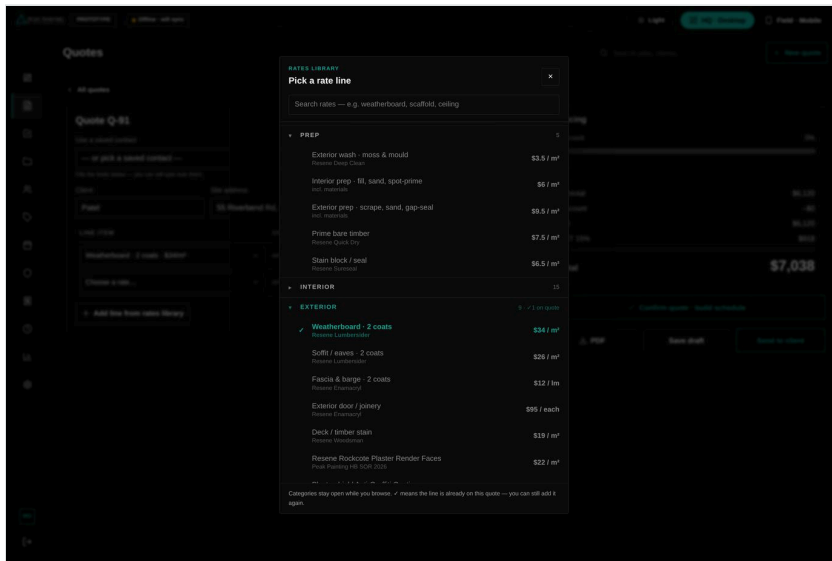

The rate picker opens with every category closed and nothing selected. Search it, or open a category. Anything already on the quote comes back ticked and in teal so you can see at a glance what you have used — you can still add it again.

THE QUOTE

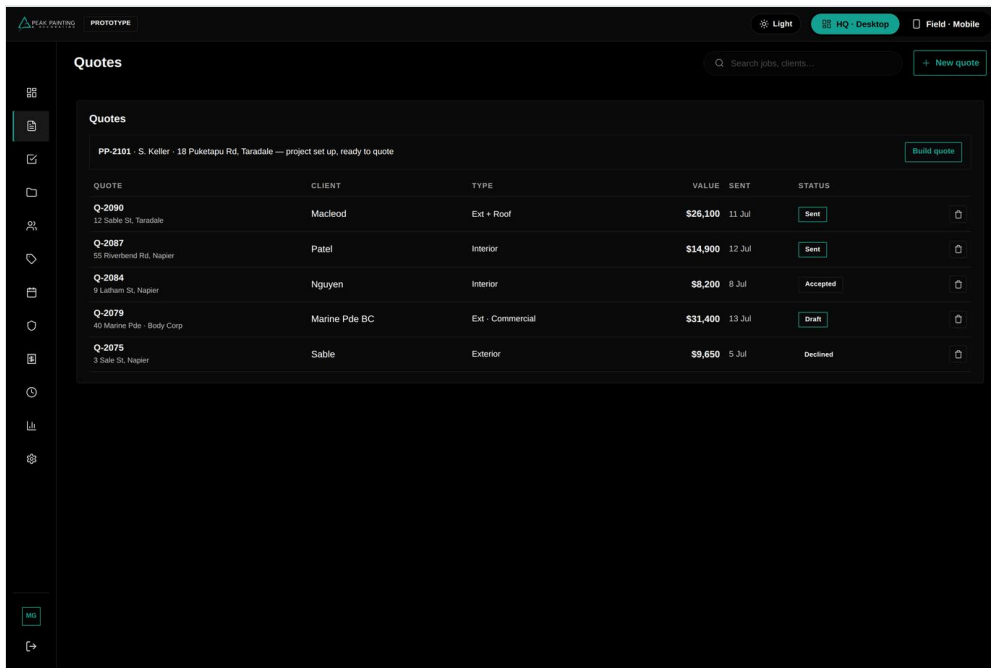


Pick a saved contact to fill client and site, or type them in. Quantity x charge-out rate = line total.

- 1 Write inclusions and exclusions in plain sentences
- 2 Download the quote PDF and send it, then set *Sent* → *Accepted*
- 3 Hit **Confirm quote — build schedule**

Your call: does the quote PDF read the way you want a Peak quote to read?

Bigger jobs, in order.

Tendering runs Details → Drawings & scope → Scope of works → Quote breakdown → Task planning → Quote summary → Paint spec. Each stage saves a revision so you can see what changed and when.

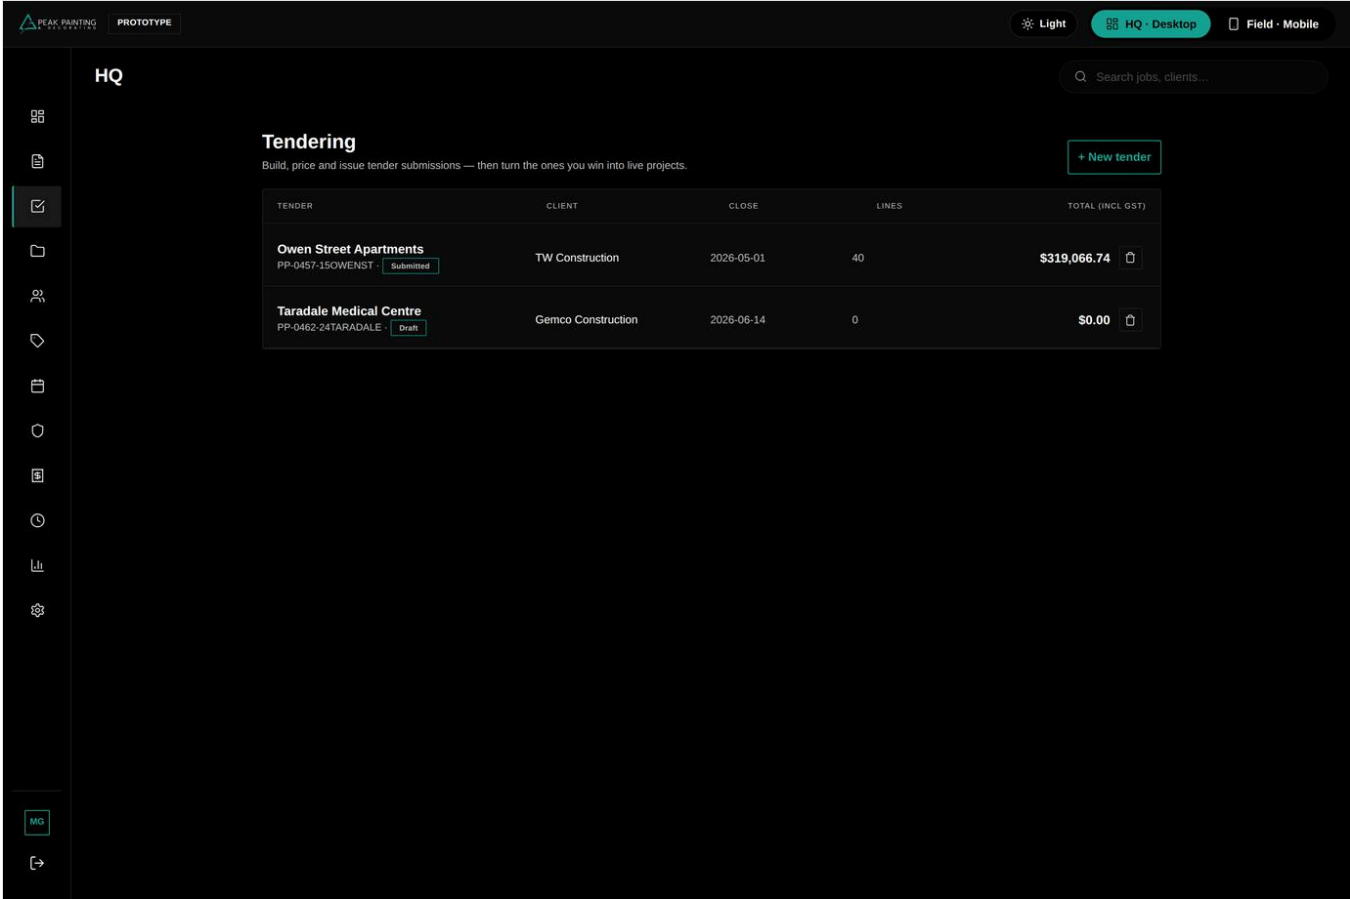


Line items drag to reorder and carry a tender group category. Drawings and paint specs open in a plan viewer you can page through.


Your call: are the tender group categories the ones your clients ask to see priced separately?

Accepted quote becomes the job.

The quote total becomes the contract value, and the task planning comes through to the schedule as the breakdown under each job.

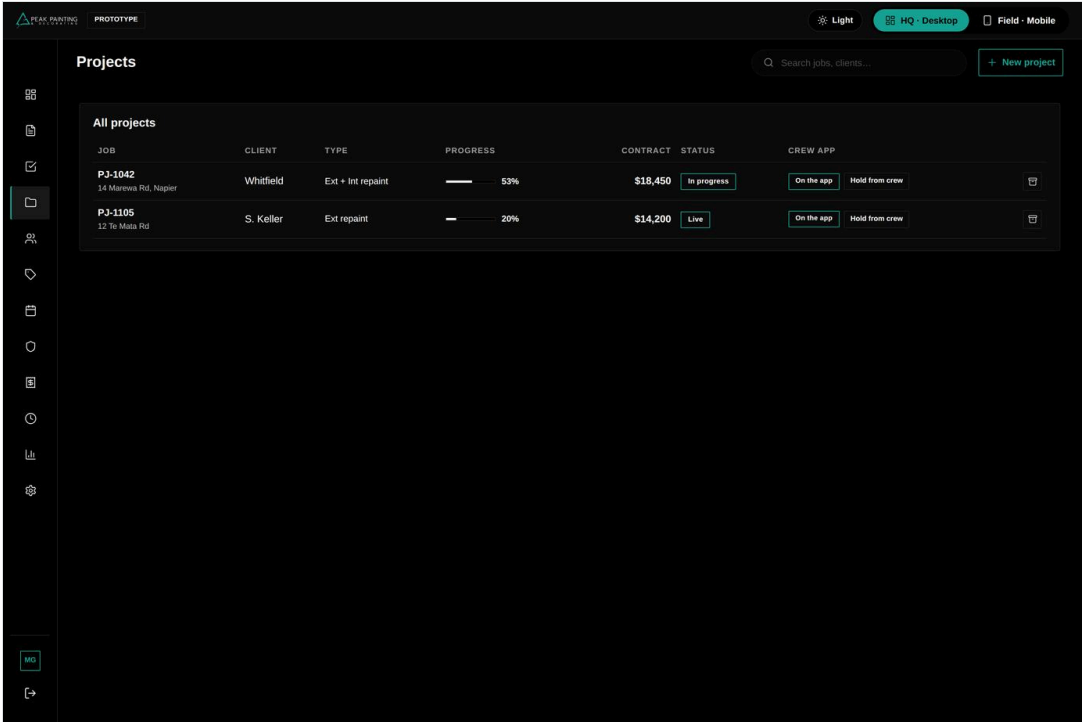

Hold from crew keeps a job off the field app until you are ready. Nothing appears on a painter’s phone until you release it.

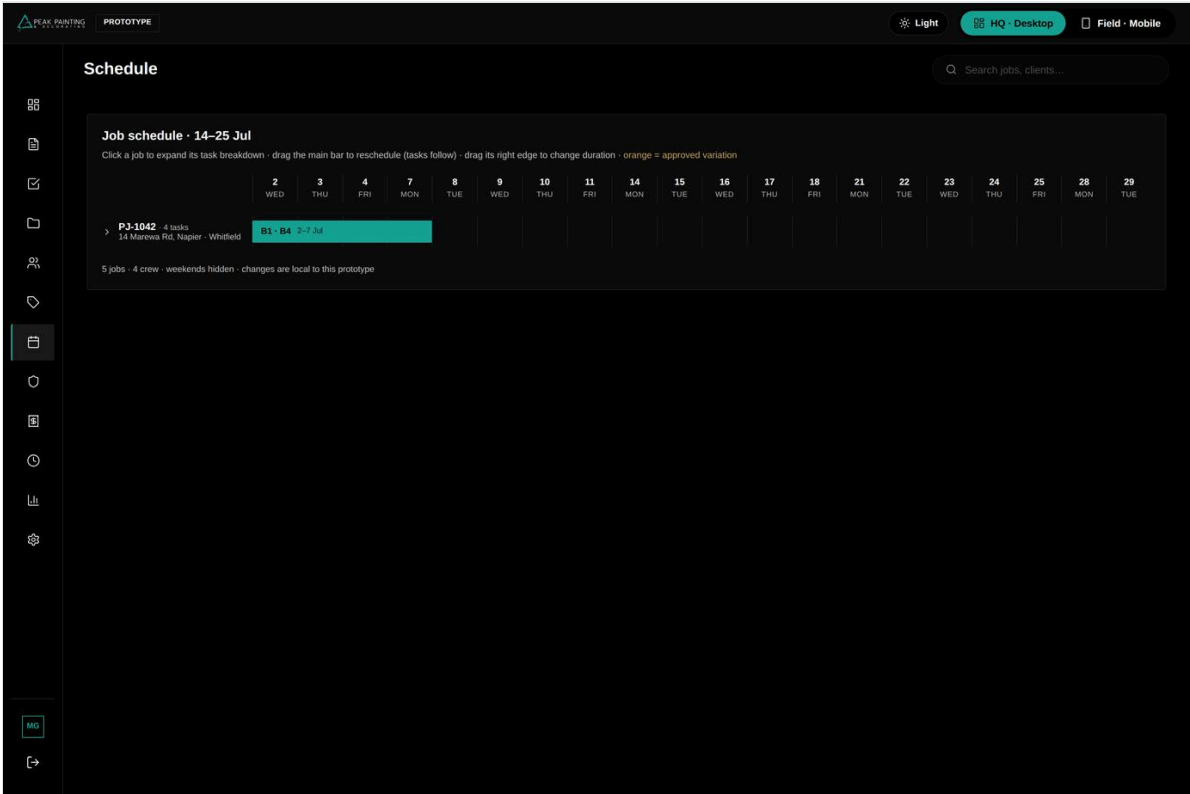


Drag the bar to reschedule; drag its right edge to change duration. Click a job to expand its tasks.

Your call: is a fortnight at a time the right window, or do you want the month?

The pack, and who signed it.

One SWMS per job, signed on the phone by each painter before they can do anything else on that job. Hazards reported on site land here.

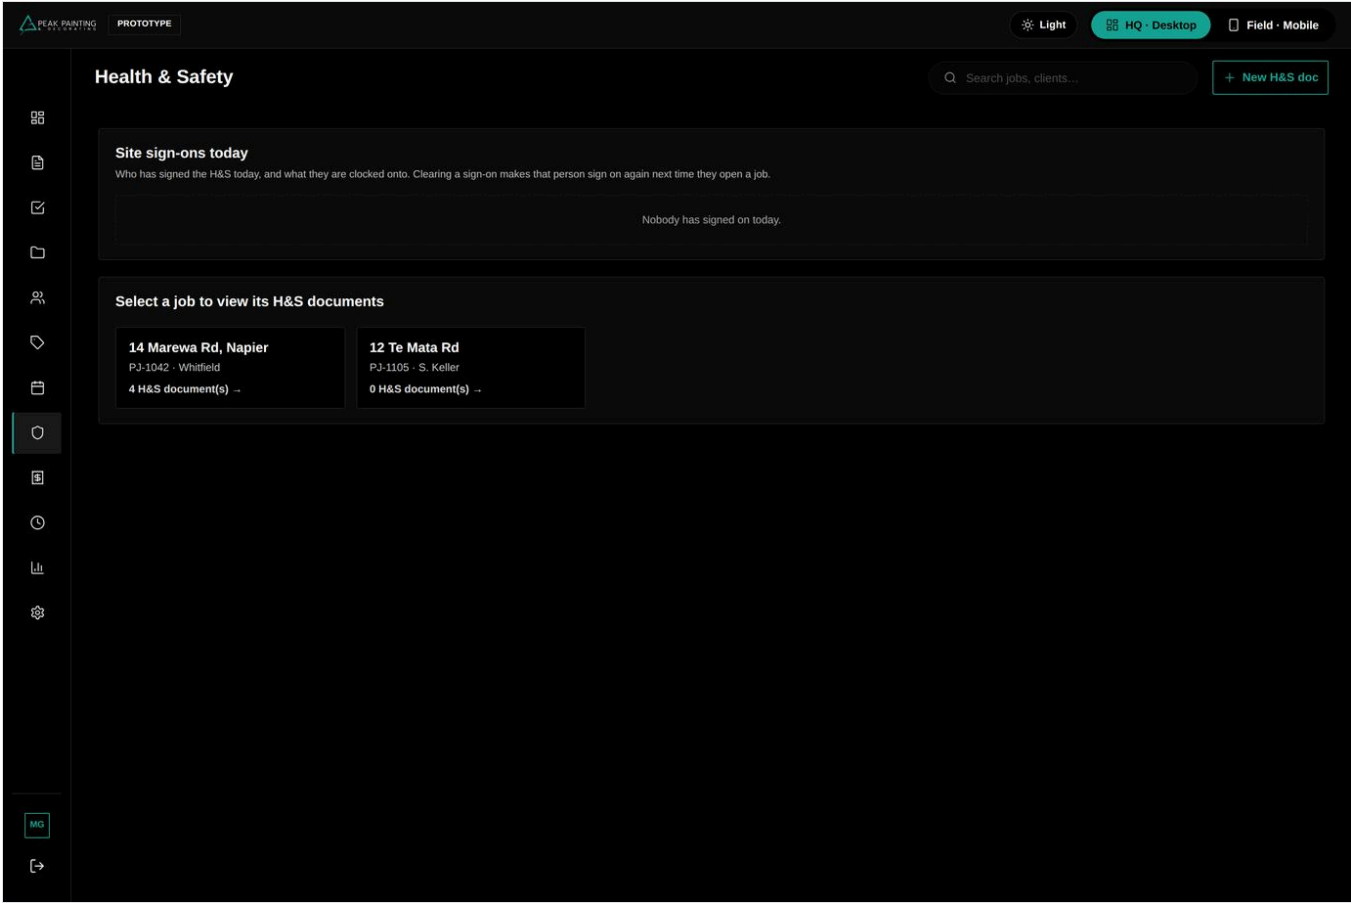


Sign-on is recorded per person per job — swap sites during the day and they sign the next one too.

Your call: does this satisfy the main contractors you work under?

Extras, then getting paid.

A painter flags a variation with photos from site. You price it from the rates library, issue it, and it only becomes work once it is approved.

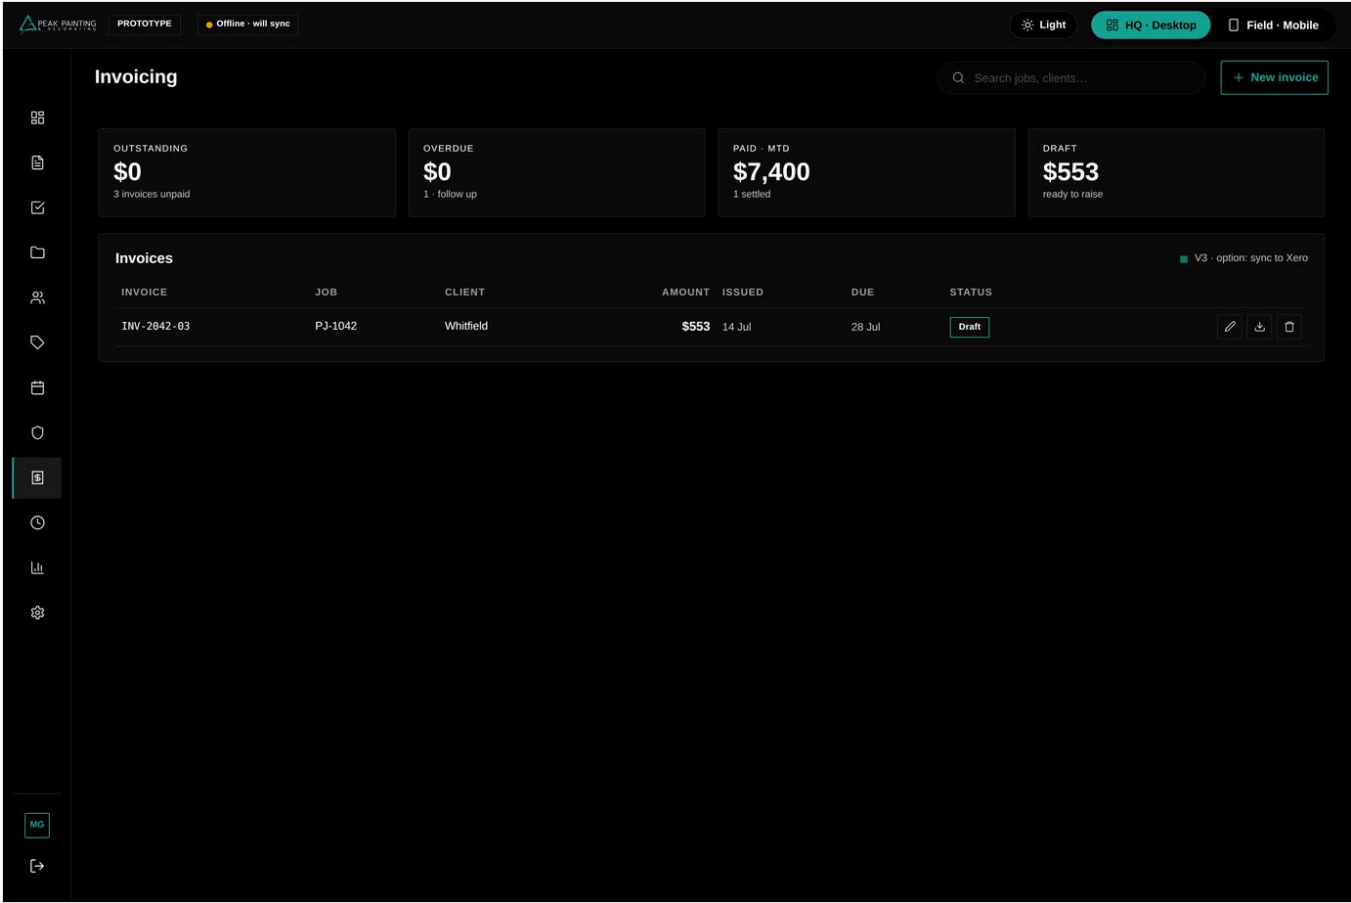

Invoices raise against the job. Anything deleted goes to Recently deleted for seven days — invoices included — so a wrong tap is recoverable.

Your call: should variations go to the client for written approval before the crew touch them?

Hours in, margin out.

Timesheets build themselves from clock-ons. Exceptions — no clock-out, no break, off-site start — are flagged for you to fix before payroll.

PEAK PAINTING

PROTOTYPE

Offline - will sync

Light

HQ - Desktop

Field - Mobile

Timesheets

Search jobs, clients...

< 31 Aug - 6 Sept >

Pay week 100 · crew submit by Fri 5pm · payroll runs Mon 9am

Remind crew

Approve all · 3

Export

TOTAL HOURS

0

0 ord · 0.0 OT

LABOUR COST

\$0

wages + OT + vehicle km

CHARGED OUT

\$0

at \$75/hr charge rate

LABOUR MARGIN

\$0

NaN% of charge out

UTILISATION

NaN%

hours billable to a job

EXCEPTIONS

0

to clear before payroll

Crew hours

Tap a row for clock-in detail

CREW	JOB	MON	TUE	WED	THU	FRI	SAT	SUN	TOTAL	COST	CHARGE	STATUS
104 Jay Harris Foreman / PM - 0 km	—	0	0	0	0	0	0	0	0	\$0	non-chargeable	Approve
105 Danny Williams Owner / PM - 0 km	—	0	0	0	0	0	0	0	0	\$0	non-chargeable	Approve
106 Ron Jeremy Apprentice - 0 km	—	0	0	0	0	0	0	0	0	\$0	non-chargeable	Approve

Overtime auto-calculated at 1.5x past 8 h/day · vehicle km at \$0.83 · approved hours post to job costing and to the payroll export.

Exceptions

clear before payroll

No exceptions this week — payroll ready. Issues appear here as crew clock in and out.

Labour budget burn

PJ-1042 · 14 Marewa Rd, Napier

58 / 132 h

0 h this week

44% · 74 h left

Budget hours come off the quoted take-off, so overrun shows up mid-job — not at invoicing.

Export to payroll, job costing, CSV or PDF.

PEAK PAINTING

PROTOTYPE

Offline - will sync

Light

HQ - Desktop

Field - Mobile

Reports & KPIs

Search jobs, clients...

COMPLETED · YTD

\$73,500

4 jobs delivered

AVG FINAL MARGIN

27%

target 30%

WORK IN PROGRESS

\$20,544

3 jobs live

VARIATIONS RECOVERED

\$4,320

extra work billed

DEBTORS OVERDUE

\$0

0 overdue invoices

QUOTES OUT

\$41,000

2 live quotes

Completed projects

final P&L

21 Chambers St

PJ-1035 · Napier City · Interior repaint

On budget

Contract \$9,800

Final cost \$6,760

Final margin 31% - \$3,038

On budget 6 days

4 Endsleigh Dr

PJ-1031 · Haweslock North · Roof + exterior

Prep overrun

Contract \$31,500

Final cost \$23,310

Final margin 26% - \$8,190

Var +\$8,190 · 15 days

12 Te Mata Rd

PJ-1028 · Haweslock North · Exterior repaint

Best margin

Contract \$14,200

Final cost \$9,088

Final margin 36% - \$5,112

Var +\$5,112 · 8 days

6 Riverbend Rd

PJ-1033 · Napier · Exterior repaint

Margin squeezed

Contract \$18,000

Final cost \$15,660

Final margin 13% - \$2,340

In progress · live

forecast

14 Marewa Rd

PJ-1042 · Whitfield · Ext + Int repaint

On track

Progress 52%

Contract \$18,450

Spent to date \$9,080

Forecast margin 30% - \$5,535

Finish 25 Jul

33 Simla Ave

PJ-1051 · Napier Hill · Interior repaint

On track

Progress 20%

Contract \$12,200

Spent to date \$2,100

Forecast margin 34% - \$4,148

Finish 1 Aug

9 Tanner St

PJ-1048 · Haweslock North · Exterior repaint

Watch - prep

Progress 78%

Contract \$9,600

Spent to date \$6,900

Forecast margin 22% - \$2,354

Finish 18 Jul

Reports show where the margin actually landed against what was quoted.

Your call: which payroll format do you need, and which KPIs do you actually run on?

Write on this page.

Anything that is wrong, missing, or not how Peak works.

THE NINE QUESTIONS, IN ORDER

- 01 PINs on both roles, or Management open?
- 02 Are the five dashboard numbers the right ones?
- 03 Are the rate lines and loadings right?
- 04 Are the access loadings close to real cost?
- 05 Does the quote PDF read like a Peak quote?
- 06 Are the tender categories the ones clients ask for?
- 07 Fortnight or month on the schedule?
- 08 Does the H&S pack satisfy your contractors?
- 09 Which payroll format and which KPIs?
